

A photograph of Millis Middle-High School. The building is a two-story structure with a prominent entrance canopy supported by dark columns. The canopy has a sign that reads "MILLIS MIDDLE/HIGH SCHOOL". The building's facade is a mix of brick and large windows. The scene is set outdoors with lush green trees in the foreground and background under a clear sky.

Millis Middle-High School

MSBA Project 2022

Statement of Interest

Spring 2021 Millis School Committee and Select Board vote to approve
the submittal of a Statement of Interest (SOI) to the
Massachusetts School Building Authority (MSBA)

June 2021 SOI submitted to MSBA citing:

- Existing overcrowding
- Expected Increase in Enrollment
- Replacement, renovation, or modernization of facility systems such as roofs, windows, boilers, HVAC, . . .
- Replacement of or addition to obsolete buildings in order to provide for a full range of programs

Eligibility Period

March 2, 2022 MSBA votes to invite Millis into the Eligibility Period


- 270 day period provides a definitive schedule for preliminary requirements
- MSBA assists with the determination of financial and community readiness
- MSBA assists with identifying needs for planning and budgeting
- 58 applicants across the state submitted SOIs
- 17 projects invited to participate in the eligibility period
- These 17 projects described as **“the most needy and urgent”**

MSBA Building Process

★ = Board Vote

Steps primarily for:

🇺🇸 = Funding Vote

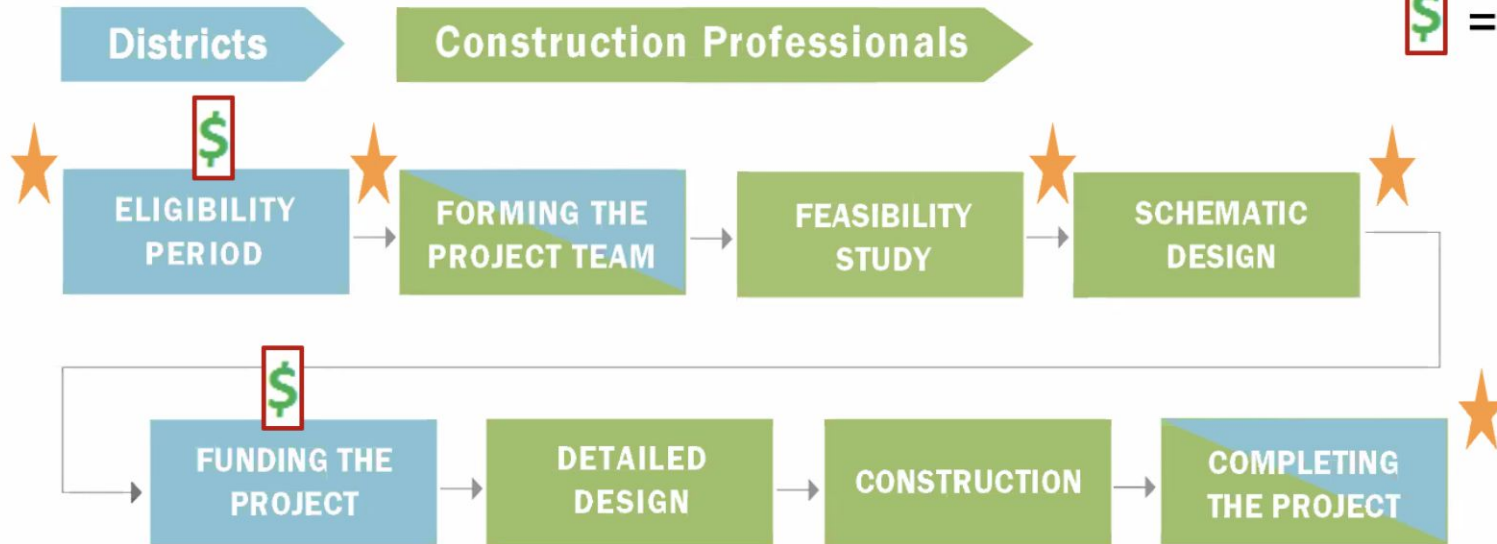

http://www.massschoolbuildings.org/building/modules_overview

**Eligibility Period
Schedule of Deliverables**

**Town of Millis
Millis High School**

MSBA Board of Directors Meeting – March 2, 2022

Eligibility Period Commences – July 1, 2022		
MODULE ONE - Eligibility Period		
Deliverable	Days	Due Date and Status
Initial Compliance Certification	30	August 1, 2022 Required
School Building Committee	60	August 30, 2022 Required
Educational Profile Questionnaire	90	September 29, 2022 Required
Online Enrollment Projection	90	September 29, 2022 Required
Enrollment/Certification Executed	180	December 28, 2022 Required
Maintenance and Capital Planning Information	180	December 28, 2022 Required
Local Vote Authorization	270	March 28, 2023 Required
Feasibility Study Agreement	270	March 28, 2023 Required
Eligibility Period Concludes – March 28, 2023		

Note: If the District has concerns about meeting any of the following deadlines, please let the MSBA know by July 1, 2022. The MSBA will require districts that are unable to complete the preliminary requirements within the timeframes noted for each to withdraw its SOI and reapply when the District has the financial and community support required.
